FOR MYSORE STATE

06 31 10 60.

Pub (Coord) (1953) Department.

Ts SERIES.

G.O. NO. 293

Dated 4. 2. 53

Passed
24/2/53

Sd/-

Ex 23/4/53

G.O at f 13 Cf

[Despatch Abstract.]

CPs — South Kanara area — Communications - estimate for the Construction of a foot bridge at Nethl in Kotekar village Mangalore Taluk — Sanction accorded.

Ref.C.No.86/53-B. Office of the Project Executive Officer,
South Kanara, Mangalore Dt. 8-1-1953.

From

Sri G.Simhadri, B.A.,
Project Executive Officer,
Mangalore.

ACCOUNTS & SPECIAL CELL (CONFIDENTIAL)
15 JAN 1953
PUBLIC (C. P.) DEPARTMENT
MADRAS

To

The Director of Community Projects and
Ex-Officio Secretary to Government,
Fort St.George, Madras 9.

.....

Sir,

COMMUNITY PROJECTS - South Kanara - Communications - Constructing a foot-bridge at Nettil in Kotekar village - Estimate - Sanction - Requested.

.....

I submit herewith an estimate in duplicate with the necessary site plan etc. for the construction of a foot-bridge across a stream at Nettil in Kotekar village. People residing in this locality have to cross this stream to go to the Railway Station, High School and the local factories. During rainy season, when the stream gets flooded, people are not able to cross it and have to take a circuitous route. A foot-bridge across the stream at this place is therefore an absolute necessity. The firka committee and the Project Advisory Committee have approved the proposal.

2. The cost of construction of the work is Rs. 1,000/- On behalf of the villagers, the Panchayat Board, Ullal has come forward to contribute 50% of the cost. The Community Project will have to bear the remaining 50%. In view of the usefulness of the work, I request that it may be sanctioned urgently subject to the above condition and the sanctioned estimate returned to me for further action.

PROJECT EXECUTIVE OFFICER.

9/1/53

Report to accompany the estimate for Constructing a foot bridge
at Nellad in Kotikan Village

This estimate provides for the construction of a foot bridge over
the Kuruvi which drains the paddy fields at Nellad in Kotikan
People residing in the near by villages will have to cross this river
when they want to go to Railway Station, High school and other
a foot bridge.

The possible site to provide a wooden foot bridge of 3'9" width
The deck portion is carried over by the longitudinal beams which
rests on standing rubble masonry piers by driving dowels.
The foundation is taken to a depth of 3'0 below ground level as
Ancient channel 1:4:8 RC plain cement concrete of grade
M 20 1:1:2 with wooden decking fixed by screws and bolts etc.
as shown in plan.

Necessary provision is also made for providing
handrails, steps etc and also for painting two
coats with

Estimated cost Rs 2500/-

26/11/52

6/1/53

Foot Bridge at Nellil

5

Design of deck planks

Clear span – 3'-6"

Dead weight $1 \times 3\text{-}6 \times \frac{1}{6} \times 50$ lbs = 29 lbs

extra for kerb hand rail etc = 6

35 lbs

Live load at 80 lb/sq ft. $3\text{-}6 \times 1 \times 80$ = 280

Total 315 or 320 lbs

Stiffness formula $= W = 150\, Bd^3/L^2$ Let "b" = 12"

$\therefore d^3 = \frac{320 \times 3\frac{1}{2} \times 3\frac{1}{2}}{150 \times 12} = 2.18$. $d = 1.296$

Hence thickness of 2" provided is quite sufficient

(2) Beam

Dead Wt of timber $= 33 \text{ cft} \times 50$ lbs = 1650

Live load $12 \times 3\text{-}9 \times 80$ lbs = 3600

5250

Load acting on one beam = 2625 lbs.

Stiffness formula $= W = 150\, bd^3/L^2$

Let $b = 6$"

$d^3 = \frac{2625 \times 12 \times 12}{150 \times 6} = 420$. $d = 7.482$'

Hence a Section of 6" × 9" provided is safe

3) Abutment :—

Dead weight of timber as above = 1650

Live load $15 \times 3\text{-}6 \times 80$ lbs = 6200

5850

Load acting on one abutment = 2925 lbs

Wt of masonry $6 \times 10\text{-}6 \times 2 + 3\frac{1}{2} \times 140$ = 26252

Concrete $14 \times 8\text{-}0 \times 5\text{-}6 \times 140$ = 6160

33337 lbs

Bearing area $= 8 \times 5\text{-}6 = 44$ sft.

P.T.O.

DETAILED ESTIMATE.

3,72,478—4-11-49. C.F. 160 (1).

District — Taluk

Village and Survey — Date and cost of original construction

Name and number of work — Date and cost of last repairs

Details of work.	Number.	Measurement in feet. Length.	Breadth.	Depth.	Area or contents.	Total quantity of each description of work.
1) Earth work excavation in all soils excepting rocks requiring blasting or firing in sides with timber lead and lifts						
For abutments	2	8-6	4-6	8-6	612	
extra on bed of stream for abutment					388	
					1000 cft	
2) Dressed hard stone in cement mortar 1:4:8						
For foundation	2	8-0	5'-6"	1-0	88	1000 cft
3) Random rubble in Cement mortar 1:6						
For abutment	2	6-0	3+1+0 / 2	8-6	281	
above beam level	2	6-0	2-0	1-0	24	
For steps below	2	7+4 / 2	2-0	2-6	55	
top	2	4-0	1-0	0-9	6	
Extra if required			— 6 —		34	
					400 cft	400 cft.
4) Pointing with Cement mortar 1:4						Deleted. inch. C.R. masonry need not be pointed separately
abutment	2	10-0	7-0		140	
For steps	2	7-0	2-6		35	
extra		— 15 —			25	
					200	
5) Langhstone dry packing						
Side of abutment	4	3-0	6-0	1-0	72	
Under slab	2	7-0	4-0	1-0	56	
					125	130 cft.
6) Best hardwood wrought and put up in new necessary nails etc complete						
Length wise beams	2	14'-0"	0-6	0-9	10.50	
Posts	5×2	2-6	0-3	0-3	1.56	
Struts	5×2	2-6	0-3	0-3	1.56	
top and sail	10×2	15-0	0-3	0-2	1.25	
Curbs	1×2	15-0	0-2	0-1½	0.63	
Kerb	2	14'-0"	0-3	0-3	1.75	
Decking	1	14'-0"	4-6	0-2"	10.50	
extra for fixing struts	5×2	2-0	0-8	0-2"	1.67	
extra for Cleats	lb	6			1.58	
					30	30.00
7) Painting with hot Coal tar 2 Coats						
Hang beams	2	15-0	2-6		75	
Posts	5×2	2-6	1-0		25	
Struts	5×2	2-6	1-0		25	
top sail	2	15-0	0-10		25	
Curbs	2	15-0	0-7½		18	
Kerbs	2	15-0	1-0		30	
Decking	1	15-0	9-6		140	
Extras			6		14.2	
					500	

8 2

C.F. 150 (1)

Details of work.	Number.	Measurement in feet. Length.	Breadth.	Depth.	Area or contents.	Total quantity each description of work.
(8) Supplying and fixing [illegible]	4				Lm.	✓
(9) Supplying and fixing Screen for ring board and [illegible]						—
(10)						
(11)						

20/10/52

6/11/52

P.W.D. Form

Statement to accompany the estimate for _____

Quantity.	Description of work.	Rate. Rs.	A.	P.	Per	Amount. Rs.	A.	P.	Total.
1)	Earth work excavation in all sorts including blasting								
1000 cft	@ Rs 20 B	21	6	-	1000 cft	21	6	-	✓
2)	Cement Mortar 1:4								
100 cft	Sand	2	8	-	100 cft	2	8	-	✓
165 lb	Cement @ 87-8	15	3	6	1 cwt	15	3	6	✓
100 cft	Sand IN MR @ 3/7 lead	36	10	6	"	9	10	8	
25 cft	Cement G MR @ 2/5 lead	3	12	-	"	3	12	-	
100 cft	Rubble Masonry					-	5	10	120-0-0
						115	12	-	120/14/-
3)	Cement Concrete 1:4:8								
100 cft	1½" metal	23	-	-	100 cft	23	-	-	
50 cft	Mortar	115	12	-	"	60	0	-	
½	Mason 2nd Class	2	12	-	each	1	6	-	
2	Men Mazdoor	1	8	-	"	7	6	-	
4	Woman "	-	12	-	"	3	-	-	
100 cft	Lead 1 M 3/5 Lift @ Lead	15	3	6	100 cft	15	3	6	
		5	4	-		7	4	-	
						-	6	6	110-8-0
						98	8	-	110/14/-
4)	Random rubble in Cement Mortar 1:4								
110 cft	Rubble stone	16	-	-	100 cft	17	9	7	
36	Mortar	120	0	-	"	40	14	5	40-11-8
5 No	Masons 1st Class	3	2	-	each	15	10	-	
4 No	Men Mazdoor	1	8	-	"	6	-	-	
4 No	Woman "	-	12	-	"	3	-	-	
110 cft	Lead as above	15	3	6	100 cft	12	6	10	
		5	4	-		4	1	4	
						-	3	11	160-8-0
						58	-	-	160/14/-
5)	Pointing with Cement Mortar 1:4								
1 cft	Mortar	120	14	-	100 cft	1	3	9	
½	Mason	115	12	-	"	2	2	6	
½	Men Mazdoor	3	2	-	each	4	11	-	
1	Woman Mazdoor	1	8	-	"	0	12	-	
		-	4	-	"	-	12	-	
						-	1	9	
						7	8	-	✓
6)	Repointing do pointing								
100 cft	Rubble stone	16	-	-	100 cft	7	9	7	
1	Mortar	3	2	-	each	3	2	-	
3	Men Mazdoor	1	8	-	"	4	8	-	
2	Woman "	-	12	-	"	1	8	-	
100	Lead as above	15	3	6	100 cft	1	6	10	
		5	4	-		-	3	11	
						22	6	-	

Data sheet to accompany the estimate for _____

Quantity.	Description of work.	Rate. Rs.	A.	P.	Per	Amount. Rs.	A.	P.	Total.
(7)	Best country wood weight and strip.								
1 cft	Cost. cutting 2	7	2	-	1 cft	7	2	-	
½	Carpenter	3	6	-	each	1	11	-	
1	Man Mazdoor	1	8	-	"	1	8	-	
1 cft	Lead 6 MR + ½ furlong 4th Class	29	15	-	100 cft	-	4	9	
							5	7	
	Sundries for nails etc					-	6	3	
						11	-	-	4/-
8).	Painting with best Coal tar 2 coats.								
8½ lbs	Coal tar	-	4	-	lbs	2	2	-	
1½	Man Mazdoor.	1	8	-	each	2	4	-	
	Sundries for Brush etc.					-	6	-	
						4	12	-	
9).	Supplying and fixing hooking down bolts 2'-0" long ¾" ø with necessary fixtures								
1	Each complete					2	-		2/-

Certified that the rates and lead for metal adopted are correct that best country wood has been used.

24/10/52
Supdt.

6/11/52
I.E.

ESTIMATE FORM — Abstract.

Item number. (1)	Quantity. (2)	Description of work. (3)	Rate. (4)	Per (5)	Amount (6)	Total. (7)
			RS.		RS.	RS.
		Earth work excavation in all sorts excepting				
	100 Cft	hard soil requiring blasting	2 1/6	100 Cft	22	
	100 Cft	Concrete broken stone in CM of ratio 1:4:8	110/8	100 Cft	111	
			95/8	100 Cft	99	
			100/8/0		300	402
400	300 Cft	Random rubble in CM of ratio 1:4	88/-	"	264	
	200	Pointing with Cement mortar 1:1	7/8	100 Sft	15	
			46/6		6	
130	100	Rough stone dry packing	33/-	100 Cft	46	58
30	33	Best Country wood wrought and put up	4/-	Cft	363	330
	500	Journey with best Coal for 2 Coals	4/12	100 Mt	24	
	4	Supplying and fixing bowling down bolts	2/-	each	8	
	Ls	Supplying and fixing 8 plates 4" & 6" & 6" Cast	Ls -		1910	
					30	
	Ls	Petty Sundries and Contingencies	Ls -		46 55	
				Total	900	
						1020/-

Sheerbutty
26/10/52
Inspection Officer
Nanjangud

Checked & Abstract Sheet
T.E. 6/1/53.

P.W.D. V-12 (Outer)—58,685—3-6-49.

(E. No. 31.

CIRCLE—

DIVISION—

DISTRICT—

TALUK (OR ESTATE IN CASE OF ESTATE WORKS).

ESTIMATE FORM—Abstract.

Financial head—

Budget head—

Departmental head—

Main head—

Sub-head—

Project of which the work forms part

Section—

Name of work— Construction of Foot Path Side at Nellad in Tottekan Village

Amount of Estimate, Rs. ~~1000~~/- 1020/-

To be carried out by—

REFERENCES.

The estimate has been Scrutinized and found in order

S. Vaikundam
Supervisor 20.1.53

Amount of Estimate Rs 1020/-
Amount of Contribution Rs 510/-
Amount of Sanction Rs 510/-

Sanctioned for Rs 510/- (Rupees five hundred and ten only)

Director, Community Projects
23/1/53

20.1.53

30/1/53

(C.NO. 901).

PUBLIC (COMMUNITY PROJECTS-II) DEPTT.

G.O. Ms. No. 293 dated 4-2-1953.

Abstract: COMMUNITY PROJECTS - South Kanara Area - Communications - Estimate for construction of a foot-bridge at Nettil in Kotekar Village - Mangalore Taluk - Sanction accorded.

...

Ref: ~~Read~~ from the P.E.O., Mangalore, R.C.No.86/53-B, dated 8-1-1953.

...

O R D E R:

Sanction is accorded to an expenditure not exceeding Rs.510/- (Rupees Five hundred and ten only) being half the estimated cost for constructing a foot-bridge at Nettil in Kotekar Village in Mangalore taluk. The other half of the estimated cost should be contributed by the beneficiaries. The Project Executive Officer, Mangalore should get the work executed according to plan and estimate sanctioned and send a completion report in due course.

2. The expenditure will be debited to "63 B.Communi Development Projects - II Community Projects - h. Communicatio ~~5 Other charges~~". (Bridge)

3. The estimate for Rs.1020/- for constructing the foot-bridge is returned herewith duly sanctioned together with the plans and sketches ~~x~~ in original.

To
The P.E.O., Mangalore.
(with encls) (By Regd Post)
" A.G., Madras.
Copy to Pub.(C.P.-Accts.)Deptt.

S.F.
S.Cs.

Note: The estimate sent by the P.E.O., Mangalore may be sanctioned, as it has been scrutinized technically and is in order. Popular contribution at 50% of the estimated cost is forthcoming. The plan and ~~duplicate of~~ the estimate in original will be forwarded to the P.E.O., Mangalore for further action. ~~Finance~~ Technical Copies of the estimate may be countersigned. ~~may see for acceptance.~~

Thro' Pub.(C.P.-Accts)Deptt.

15

Public (Community Projects-Audit) Dept.

7982

Memorandum No. Public (C.P.Audit)/53- 1 d/-24 A 53

Sub:- Community Projects - South Kanara area - Communications
Construction of a foot bridge at Nethl in Kotekar Village
Mangalore Taluk - Completion report

Ref:- G.O.No.Ms.293 Public (C.P.) Department, 4.2.53

The Project Executive Officer, Mangalore is requested to expedite the submission of the completion report called for in the Government Order cited.

To the P.E.O.,
Mangalore

(R.D. & ~~weeks~~ months)

Note.- P.T.O.

Note.-

The draft memo. put up above may be approved, as the completion report due from the P.E.O., Bangalore has not been received yet.

9993



Ref.C.No.86/53-B. Project Executive Office, S.
Mangalore, Dated 6-5-195

From

Sri C.Simhadri, B.A.,
Project Executive Officer,
Mangalore.

To

The Director of Com
and Ex-Officio Secretary to Gove
Fort St.George, Madras 9.

Sir,

Sub: Community Projects - South Kanara area - Communications - Construction of a foot-bridge at Nettil in Kotekar village - Completion report.

Ref: Govt.Memo.No. 7932 Pub.(S.P.Audit)/53-1 D/21-4-53.

In this case, the Panchayat Board, Ullal has promised 30% contribution and it was proposed to entrust the work to it for execution. But the Board could not take up the work on account of an order issued by Government directing Panchayat Boards not to incur any expenditure on new works until the elections are over. In this connection, kind attention is invited to this office report Ref.C.No.157/52-B dated 6-4-1953 and D.O.letter Ref.C.No.157/52-B dated 2-5-1953 to the Dy. Secretary to Government. On receipt of orders permitting the Board to incur expenditure on the work, the work will be taken up and completed expeditiously and the completion report submitted.

Thro C.P.W.

Public (C.P. Audit) Sept

To Govt 30-6-53

F/7.5.

PROJECT EXECUTIVE OFFICER.

P.C.-

Public (CP III)

~~Gen Pts.~~

With Ref to A on P 3 above
L A have proposed to issue Revised
orders in this matter. The orders will
issue in a day or two.
When the orders are received from L.A. Comm. calls
Copies to all P.E.Os. Also send some 4 addl.
spare copies to each P.E.O. to enable him/her
to Communicate it to the APOs

15/7/53

The instructions are
noted.
15/7/53

Gen. Registry
dt. 30-6-53.
30/6

7982 Public (CP. Audit) 1531 dt. 24-11-53.

C.F. 98 Public (Community projects) DEPARTMENT 21515

Audit

REMINDER. OFFICE OF THE Project Executive Officer, Mangalore

PROJECT JUL 1953 AUDIT BRANCH

Please the honour to invite attention to my letter

and am directed to invite

Ref. No. C no. 86/53-B dated 6-5-1953.

~~to request that the reply to it may be expedited~~

request that this reminder may be returned at once with information as to—

(1) the stage at which the matter now is,

(2) the date by which a reply may be expected, and

~~(3) the circumstances which have caused the delay~~

Office of the Director of Community projects

Station Post of. Cottage Madras-9.

Dated 30-6-53.

Signature. for

Designation. Dy. Accounts Officer, Special Officer.

SUBJECT. C.P.S. - South Kanara area - Public (C.P.) Dept. Communications - Construction of a foot-bridge at Nettilin Kotekar village - Completion report.

12,84,021—11-10-51

520 15.7.53 C.F. 98.

RA. 15.10.53 REPLY.

To The Director of Community Projects
No. 1379 and Ex-officio Secretary to
15/7 Government. Y.S.G. Madras

Sir, The masonry work has been completed and decking is in progress. The work will be completed as expeditiously as possible and the completion report submitted.

CA 826.8.53
RA 16.9.53

Director of Community Projects & ex-officio Secretary to Government

Public (C.A. Unit)

N.R. 15/8/53

15/7

E 14/7/53 16 14/7 9/8/53

7982/53 — 21

G.F. 93 Public Works DEPARTMENT.

REMINDER C.P. (Audit) Branch.

To THE Project Executive Officer Mahgaleva.

PROJECT EXECUTIVE 19 SEP 1953 MAHAGALOYA

I ~~have the honour to invite~~ ~~am directed to invite~~ invite attention to your

Ref No. 86/53-B, dated ~~15/9/53~~ 6.8.53 and to request that the reply to it may be expedited

request that this reminder may be returned at once with information as to—

✓ (1) the stage at which the matter now is,

✓ (2) the date by which a reply may be expected, and

~~(3) the circumstances which have caused the delay.~~

Office of the Director Community Projects (COMMUNITY PROJECTS) Signature.

Station Fort St. George 28 SEP 1953 Accounts Officer

Dated 15/9/53 Designation.

C-P.S. South Kanara area - Construction of a foot bridge at Nettiki in Mokeka village — Completion report.

(P.T.O.

1,682,131—15-11-52.

C.F. 93.

27183 REPLY.

To The Directors of Community Projects
& Ex-officio Secretaries to Govt
Madras.

Sirs,

The work has been completed and the final payment made. A separate Completion report will be submitted in the matter at an early date separately.

Public (P.A. Dept)

MAR. 25/10/53

Project Extension Officer

27/10/53

R.D. 26/10/53

R.D. 26/10

Very Urgent

C.F. 98- Public (CP Audit) DEPARTMENT.

EXECUTIVE OFFICER PROBATION OFFICER MANGALORE

REMINDER. _____ Branch.

To The Project Executive Officer, Mangalore.

~~has the honour to invite~~ I am directed to invite attention to Memo No. 7982 Pub(CPAudit)53-1. dated 24-4-53. Yours and Ref 86/53 dated 24.9.53

~~to request that the reply to it may be expedited~~ request that this reminder may be returned at once with information as to—

(1) the stage at which the matter now is,

(2) the date by which a reply may be expected, and

(3) ~~the circumstances which have caused the delay~~

Office

Station

Dated 26/10/53

Signature.

for ACCOUNTS & SPECIAL OFFICER, (COMMUNITY PROJECTS.)

Designation.

PUBLIC (CP) DEPARTMENT.

SUBJECT.

CP 3 - South Kanara area - Communications - Construction of a foot bridge at Nettil in Kotekar Village - Mangalore Taluk - Completion Report.

(P.T.O.

1,682,131—15-11-52.

ACCOUNTS & COMMUNITY PROJECTS
4 NOV 1953
PUBLIC (C. P.) DEPARTMENT
MADRAS

C.F. 98.

REPLY. 29443 4/53

To The Director of C.P. and
Ex officio Secretary to Govt
Madras. 9.

Sir,

The work has been completed and the completion report is submitted separately.

Agn (CPan&N).

For R.D. Mangalore
in charge

NR 30/10
11-12-53
Ab
DAILY 10/11/53 9/DL/53

31/X

ACCOUNTANT & SPECIAL OFFICER. (COMMUNITY PROJECTS.)
2 DEC 1953
AGRICULTURE (C. P.) DEPT. MADRAS.

31657

25.5

Ref.C.No.86/53.

Project Executive Office, S.K.
Mangalore, d/- 26th November, 1953

From

Sri H.Narasimha,
Project Executive Officer,
Mangalore.

To

The Director of Community Project
Agriculture (C.P.) Department,
Fort St.George, Madras 9.

.....

Sir,

Sub: Community Projects - South Kanara - Communications
Construction of a foot bridge at Nettil in Kotekar
village - Completion - Report submitted.

Ref: G.O.Ms.No.293 (C.P.) Department dated 4-2-1953.

.....

I am herewith submitting the completion report along with the site plan in respect of the construction of a foot bridge at Nettil in Kotekar village in Mangalore Taluk, sanctioned in G.O. cited above. The total cost of the work amounted to Rs. 889-2-0, out of which Rs. 444-9-0 represents the Government share, the balance of Rs. 444-9-0 being the value of the contribution.

H Narasimha 27/11/53

PROJECT EXECUTIVE OFFICER.

Copy submitted to the Accountant General, Madras with the copy of the Completion Report.
T/27.11.

27/11

Name of work :- Construction of a foot bridge at Nettiku in Kolekadi village Est Rs 1020/- Sanct Rs 510/- G.O No

G. O M.S No 293 (C.P.) Community Project Dept dt 2/53 DEPARTMENT. South Kanara Mangalore. C.F. 296

Completion Report.

Estimate.	Date of Commencement. (2)	Date of Completion. (3)	Passing by the (4)	Particulars. (5)	As estimated. Quantity. (6)	Rate. (7)	Amount. (8)	As executed. Quantity. (9)	Rate. (10)	Amount. (11)	Difference (excess to be shown in red ink). Quantity. (12)	Rate. (13)	Amount. (14)	Explanation for the difference. (15)
	6/53	7/53		1) Earth work excavation in all soil except Rock requiring Blasting ..	1000 cft	Rs. 21 6 0	Rs. 22 0 0 ~~21 6 0~~	776 cft	Rs. 21 6 0	Rs. 16 9 0	224 cft	Rs. A. P.	Rs. 5 7 0 ~~4 13 0~~	Fund adjustable to mechanical Excavation found sufficient
				2) Cement Concrete 1:4:8 work 1½" size Broken metal	100 cft	110 8 0	111 0 0 ~~110 8 0~~	92 cft	110 8 0	10 1 10 0	8 cft	— — —	8 14 0 9 6 0	do —
				3) Random Rubble masonry in Cement mortar 1:4	400 cft	100 8 0	402 0 0	366 cft	100 8 0	367 13 0	34 cft	— — —	34 3 0	do —
				4) Best County Wood wrought and put up	30 cft	11 0 0	330 0 0	29.31 cft	11 0 0	322 7 0	0.69 cft	— — —	7 9 0	do —
				5) Tarring with Coal tar 2 Coats --	500 sft	4 12 0	24 0 ~~23 12 0~~	33 55 sft	4 12 0	15 15 0	165 sft	— — —	8 1 0 ~~7 13~~	do —
				6) Supplying and fixing Hobolt down bolt against	4 no	2 0 0	8 0 0	4 nos	2 0 0	8 0 0				
				7) Rough slate any pattern for revetment -- ..	130 cft	44 6 0	~~58~~ 0 0	128 cft	44 6 0	56 12 0	2 cft	— — —	1 4 0 10 0 6	Found sufficient Found not necessary
				8) Supplying fix in Sqrs	L S	— — —	10 0 0	—	— — —	— — —	—	— — —	30 0 0	Not calculated
				9) Extra for Bulks and voids	LS	— — —	30 0 0	—	— — —	— — —	—	— — —	55 0 0	— do —
				10) Petty Supervision and Contingency charges	LS	— — —	55 0 0 (1050) = 1053	—	— — —	89 2	—	— — —	160 14 -	

1020/-

Total ..	819	2
Amount actually paid from CP fund ~~Amount paid~~ ..	444	9 -
Value of contribution by beneficiaries ~~Amount of 15 per cent deductions withheld~~ ..	444	9 -

Dated 23/11/ 1953.

S. Bhavanji
Designation. Supervisor C-1 Mangalore

Certified that I have examined the work from time to time whilst in progress and that it has been executed in a substantial and satisfactory manner as regards materials and workmanship and that it corresponds with the exemption noted above with the sanctioned plan and estimate.

Project Executive Officer 26/11/53 Mangalore

Revised Sanctioned Plan 1020

23/11/ Designation. Asst Engineer Community Projects S. K. MANGALORE.

Designation. Project Officer 25/11 Deck.

75,452—19-11-52.

FROM

THE

TO

THE

Madras.

Dated 19

Despatched

Bill No. of 19 -19 .

Work :—Estimate No. for

Authority—

How executed { ~~Contract~~ / Piece-work / ~~Daily labour~~

No. and page of the Measurement Book in which the items are recorded. { 16 68 / MBNo 9 }

Instructions.

This form should be submitted to with the progress report of the month in which the completion of the work is reported, care being taken that the entries in it agree with the entries in the progress report and in the Measurement Book and with the vouchers submitted.

2. It should exhibit clearly any deviation made from the sanctioned estimate and the purpose for which the amount provided under Contingencies has been utilized. The total amount payable on the work turned out, the sum actually *paid* and 15 per cent deductions withheld should be indicated.

3. The officer in paragraph 1 should check the details when he passes the work correcting, if necessary, the quantities entered under column "As EXECUTED" in red ink. He should also see whether the entries in the report accord with those in the Measurement Book and the Nominal Roll.

4. After the work is passed the officer in paragraph 1 will sign the certificate at the foot of the form with any remarks he may have to offer and despatch the report with the sanctioned estimate forthwith to the Board. *Facsimile* signatures should not be used in the certificate.

5. In the case of maintenance work as upkeep of platforms and the like in the Salt Department, the officer in paragraph 1 must see that the sanctioned scale has been adhered to and that the allotment has been properly utilized.

Certified that the work has been executed as per the Sanctioned plan and Estimate

Certified that no materials are out-standing from the Contractor in this bill

Certified that no liability is due to the Contractor from this bill

S. Bhanuji Rao
Superintending Engineer
23/11/52

Plan & The Proposed Foot Bridge at Nethil in Kotekar Village.

Scale 1/50

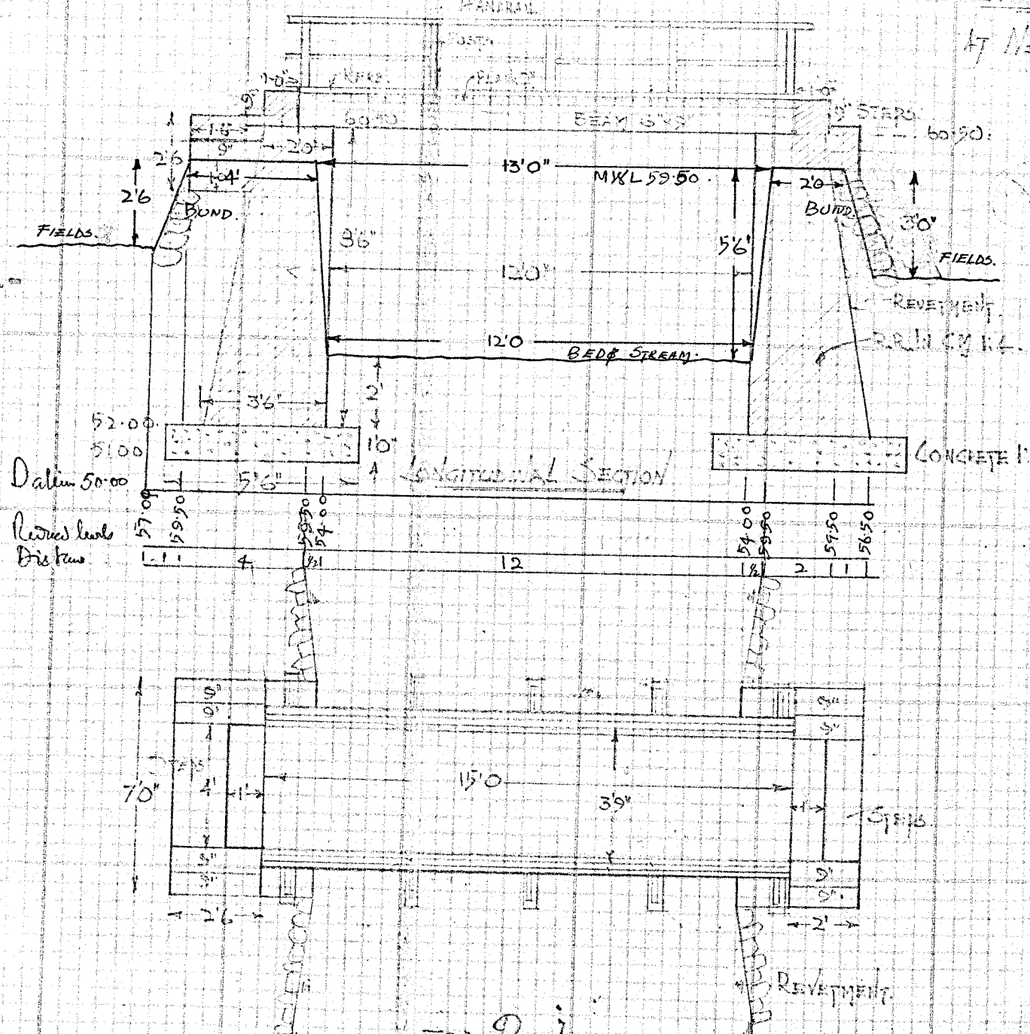

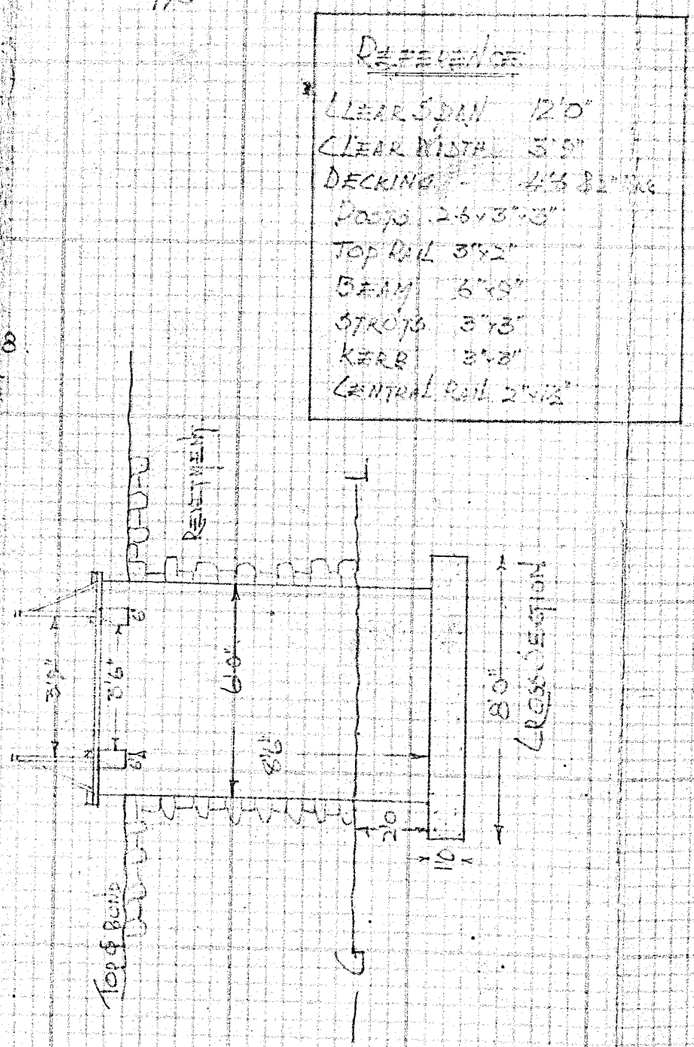



Certified that the work has been executed as per sanctioned plan and Estimate

S. Bhanuraja
Supervisor Gr I
Mangalore
26.10.92

Asst Engineer Gr II
9.12.92

Assistant Engineer,
Community Projects,
D.K. MANGALORE.

[C.No. 7982/53]

Sub:- Community Projects - South Kanara Area - Communications - Construction of a foot-bridge at Nettil in kotekar village of Mangalore Taluk - Completion plan & report -

---

Ref:- From the P.E.O., Mangalore, Ref. C.No. 86/53 dt. 26-11-53.

Please see the letter from the P.E.O. Mangalore at p:11 c.f. - He has submitted the Completion report & the Completion plan in respect of the work of Construction of a foot-bridge at Nettil in kotekar village, sanctioned in G.O. Ms. No. 293 Part dated 4-2-53. The expenditure sanctioned was Rs 510/- at half of the estimated cost of Rs 1020/-. The total value of work done as per the Completion report is only Rs 889-2-0 and the amount spent from C.P. Funds Rs 444-9-0, which is in the same proportion as the amount sanctioned to the estimated cost. No deviations from the sanctioned proposals have been done, and the quantities under the several items as per the works turned out, are also within the estimate provision. The Completion report has been checked and found to be in order. It may be accepted. The Completion certificate is also recorded on the plan. The papers may be lodged and added to the G.O. at (Q) -
